


Weekly Dashboard 10.27-11.02

Task Status

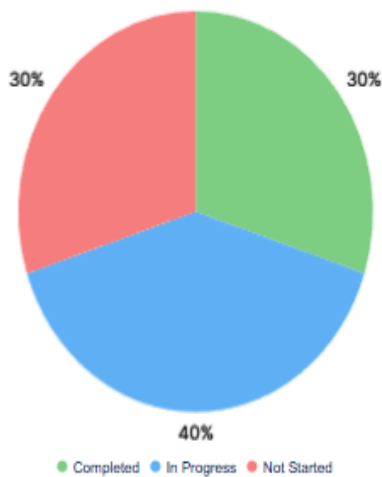

Weekly Tasks Overview

Task Name	Status	WBS ID	Assigned To
Total		Count	10
Status Completed		Count	3
Setup Backend Framework (Typescript)	Completed	2.1.1	Serena Chen
Create Employee Dashboard (Upcoming Shifts)	Completed	2.2.2	Serena Chen
Create Employer Dashboard (Add/Edit Shifts, etc.)	Completed	2.2.3	Serena Chen
Status In Progress		Count	4
Develop Web Application	In Progress	2	Benedict Astan, Gamuchirai Mhere, Serena Chen
Backend Development	In Progress	2.1	Benedict Astan, Spencer Stephen
Front-end Development	In Progress	2.2	Gamuchirai Mhere, Serena Chen
Front-End Development Report	In Progress	2.2.8	Gamuchirai Mhere, Serena Chen
Status Not Started		Count	3
Develop Restful API Endpoints (Postman)	Not Started	2.1.3	Spencer Stephen
Implement User Authentication (Login/Logout)	Not Started	2.1.4	Benedict Astan
Create Payroll Calculation Logic	Not Started	2.1.8	Benedict Astan

Decisions Log

Requested By	Serena
Date Submitted	02/11/25
Change Type	Assignee Change
Change Details	backend implementation tasks redistribute

Changes in Deadlines

Task Name	Setup Backend Framework (Typescript)
Task ID	2.1.1
Original Deadline	18/10/25
New Deadline	24/10/25
Reason	Delay caused by reassignment from Spencer to Serena.
Impact on other deadlines	Medium (Minor Delay)
Specific Impacts, Solutions, and Extra Notes	impacted backend implementation progress

Changes in Scope

Changes in Scope	none for this week
------------------	--------------------

Issues and Mitigations

Issue Number	1
Issue	Backend Development Delayed
Description	Backend development is still delayed meaning that integration with completed frontend components may be delayed as well.
Mitigation	Urge assigned team members to complete given tasks or to communicate if unable to so that other team members may help
Issue Number	2
Issue	Poor Communication
Description	Communication among team members is still poor and messages often go unreplied to. Scheduled team calls are not answered
Mitigation	Ask team members to communicate more frequently

Risks and Mitigations

Risk Number	1
Risk	Frontend Prototype Video
Description and Impacts	Due to poor communication among team members, it is unclear if the frontend prototype video for the executives will be completed on time.
Mitigation	The frontend components are mostly done so it is just a communication issue, which if resolved, will allow us to shoot the video and present it on time
Risk Number	2
Risk	Backend Development
Description and Impacts	Backend development still being incomplete may delay the project
Mitigation	The whole team must step in to help with tasks where possible to ensure we complete the project on time
